

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	Total Float
-------------	----------------------	----------	-------------	--------------	-------------

2010												2011												2012				
D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A

John N. Hardee Expressway

PHASE # II

STAGE MILESTONES

COMMENCEMENT DATE

1A00001005	SCDOT LETTING	0	17FEB10*		0
1A00001010	NOTICE TO PROCEED FIRST CHARGEABLE DAY	0	21APR10		0

MOBILIZATION

1A00001015	PRECONSTRUCTION CONFERENCE	0	14APR10		8
1A00001020	CONTRACTOR SUBMIT SHOP DRAWINGS	45	14APR10	16JUN10	8
1A00001035	OBTAIN PERMITS & ANY PERMISSION	45	21APR10	23JUN10	23
1A00001055	SHOP DRAWING APPROVAL	60	21APR10	15JUL10	8
1A00001040	CONTRACTOR MOBILIZE	8	23APR10	04MAY10	14
1A00001045	PLACE TEMPORARY STAGE I MOT	5	23APR10	29APR10	18
1A00001050	PLACE TEMP PLASTIC DRUM BARRICADES	1	23APR10	23APR10	18
1A00001025	INSTALL CONSTRUCTION MOT SIGNS	5	28APR10	04MAY10	244
1A00001030	PROJECT LAYOUT	15	28APR10	18MAY10	0
1A00001065	OBTAIN & DELIVER STEEL H PILES	5	12MAY10	18MAY10	8
1A00001085	CAST & DELIVER PC PILES	30	12MAY10	23JUN10	310
1A00001075	CAST & DELIVER PC BRIDGE BEAMS	180	03JUN10	16FEB11	224

PROJECT DURATION/PROJECT COMPLETE

1A10001000	PROJECT COMPLETION / DURATION (CALENDAR DAYS)	668*	21APR10	17FEB12	0
1A10001010	SUBSTANTIAL COMPLETION	0		17FEB12	0

I-26 EAST / WEST & JHEXW

CONSTRUCTION - ROADWAY

EARTHWORK

PREPARING RIGHT OF WAY

CLEAR AND GRUB

1A20061000	PLACE SILT FENCE	4	30APR10	05MAY10	20
1A20061010	CLEAR & GRUB WHOLE PROJECT	10	30APR10	13MAY10	14
1A20061020	REMOVE TOPSOIL WHOLE PROJECT	5	07MAY10	13MAY10	14
1A20061030	PLACE MOT BARRELS E & WB	1	19MAY10	19MAY10	0
1A20061040	DEMO EXISTING IMPROVED PROPERTY	20	19MAY10	16JUN10	191


REMOVE EXISTING PAVEMENT

1A20011005	REMOVE EXISTING I-26 (E&W) SHOULDERS	10	20MAY10	03JUN10	0
1A20011015	REMOVE EXISTING I-26 (E&W) SHOULDERS @ DUNBAR	4	04JUN10	09JUN10	6

GRADING

EMBANKMENT

1A23011005	UNCLASSIFIED EXCAV	200	04JUN10	17MAR11	0
1A23011020	PLACE EMBANK on EXP to CONNECTOR	55	18JUN10	03SEP10	0
1A23011030	CONSTR CONN to DUNBAR WITH @ GRADE X,ING	92	07SEP10	17JAN11	0

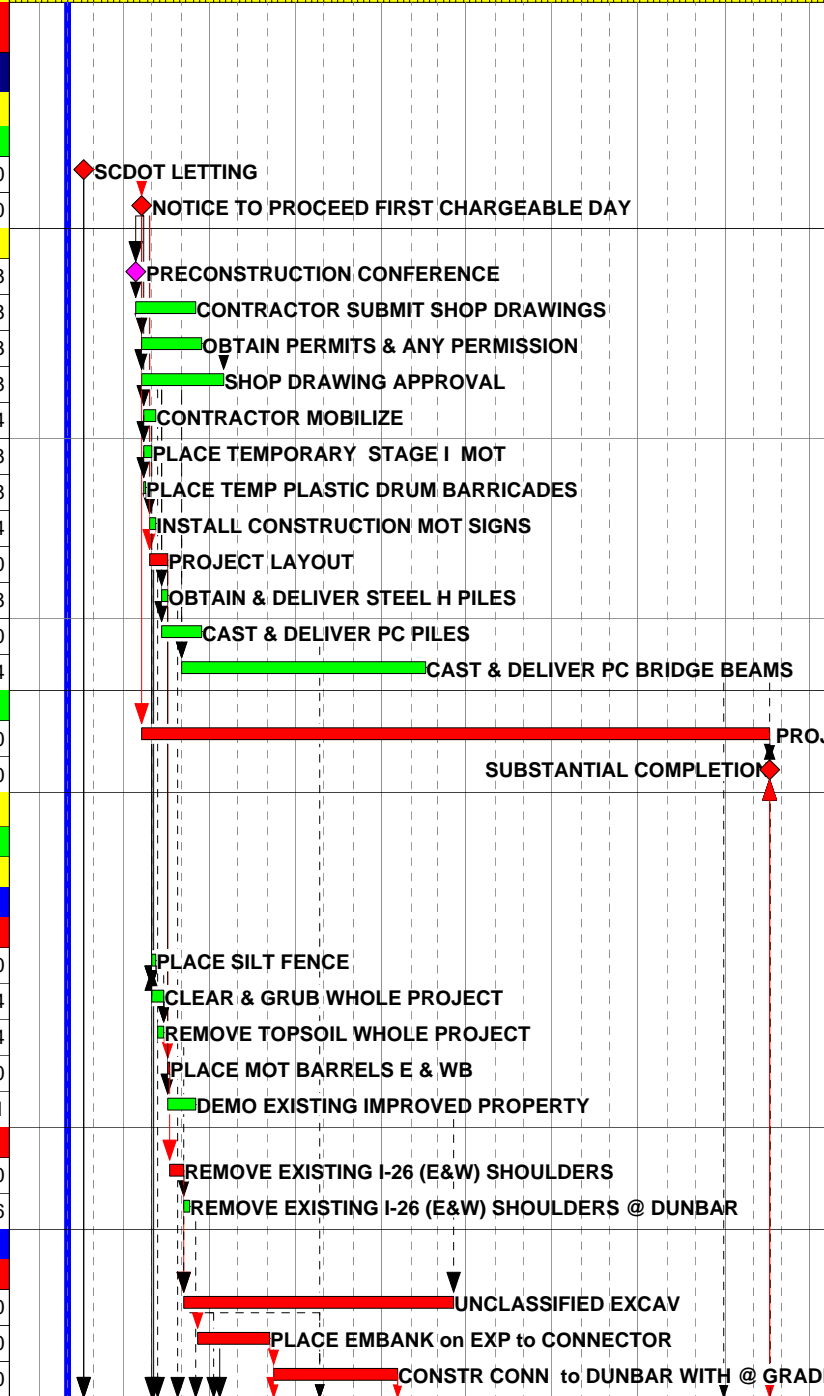

Start Date 01FEB10
 Finish Date 17FEB12
 Data Date 01FEB10
 Run Date 31AUG09 10:41
 © Primavera Systems, Inc.

Legend:
█ Early Bar
█ Progress Bar
█ Critical Activity

I26B John N. Hardee Expressway
 Tiger Grant
 DRAFT Construction Schedule
 Sheet 1 of 4

Date	Revision	Checked	Approved

